

Waite Park Project **update**



September 14, 2018

Please note that construction schedules and operations are controlled by the contractor and are subject to change based on weather and construction progress.

Stage Locations (see page 3 for map)

- Stage 1:** Pierce St NE, Fillmore St NE, Taylor St NE from 35th to 33rd Ave NE, 34th Ave from Taylor St NE to Buchanan St NE, and 35th Ave NE from Benjamin St NE to Stinson Blvd NE
- Stage 2:** Lincoln St NE and Buchanan St NE from 31st-33rd Ave NE, and 32nd Ave from Johnson St NE to Pierce St NE
- Stage 3A:** Lincoln St NE and Buchanan St NE from 33rd-35th Ave NE, 34th Ave NE from Buchanan St NE to Johnson St NE
- Stage 3B:** 36th Ave NE from Cleveland St NE to Stinson St NE
- Stage 4A:** Ulysses St NE from 33rd Ave NE-34th Ave NE, Garfield St NE from 34th Ave NE-33rd Ave NE, 34th Ave NE from Johnson St NE to Garfield St NE
- Stage 4B:** Ulysses St NE from Johnson St NE to 34th Ave NE, Arthur St NE from 33rd Ave NE to dead end
- Stage 5:** McKinley St NE from 32nd Ave NE-St Anthony Parkway, 31st Ave NE from Benjamin St NE to Stinson Blvd NE, Benjamin St NE from 30th Ave NE to 29th Ave NE, Brighton Ave NE from St Anthony Parkway to 29th Ave NE, and Brighton Ave NE from McKinley St NE to dead end at NE Stinson Blvd
- Stage 5B:** 30th St NE from Benjamin St NE-Stinson Blvd NE
- Stage 6:** 36th Ave NE from Johnson St NE to Cleveland St NE, and Hayes, Wilshire, and Garfield St NE from 36th Ave NE to 34th Ave NE

Week of September 10

Stages 1, 2, 3A, 3B, 4A: Diamond grinding and joint sealing will occur at a later date. Residents will receive a paper notice at their door before this work begins.

Stage 4B: Concrete removal and replacement concluded and the roadway was reopened to traffic.

Stage 5: Preliminary sawcutting concluded, and concrete removal and replacement continued throughout the week.

Stage 6: Preliminary sawcutting began.

Week of September 17

Stages 1, 2, 3A, 3B, 4A, 4B: Diamond grinding and joint sealing will occur at a later date. Residents will receive a paper notice at their door before this work begins.

Stage 5: Concrete removal and replacement is scheduled to continue throughout the week.

Stage 6: Preliminary sawcutting will continue throughout the week.

Saturday Work

During construction in your area, the project contractor may be working Saturdays from 9 a.m. to 6 p.m. Any complaint regarding this work can be received by Minneapolis Information and Services at 612-673-3000 or 311 for phones with a 612 area code. You can also contact the project contact listed below.




Parking & Access Information

- **Stages marked with Road Closed signs are closed to all traffic and parking 24 hours a day.** Please use alternate side streets or alleys for access. Please note that the penalty for entering work areas marked with road closed signs is a \$300 fine.
- **Stage 5:** During concrete removal and replacement, roads will be shut down to traffic, and no parking will be allowed at any time until barricades are removed. It is recommended that you utilize your back alley to access your driveways or park your vehicle(s) along adjacent side streets during this time.
 - One-way access will be allowed after working hours for those on Brighton St NE and McKinley St NE from 29th Ave to St Anthony Pkwy, and Brighton Ave from McKinley St to the eastern dead end. No street parking in the red highlighted areas will be allowed at any time.
 - Driveways that come directly into the construction area may be closed for a short time (up to 4 days) if concrete work occurs directly in front of your driveway. You will be notified one day in advance before this occurs with a paper flyer in your door. It is recommended that you park your vehicle(s) along adjacent side streets during the time of your driveway closure.
 - Phase 5 is anticipated to take about 3 weeks to complete. Please note individual blocks will be closed within the phase and reopened as the contractor completes certain areas.
- **Stage 6:** Please do not park on the roadway from 7 a.m. to 6 p.m. during preliminary sawcutting.

Thank you for your patience throughout this process! If you have any concerns, please contact the representative listed below.

NICOLE SCHMIDT

Project Information Contact
nicolesc@bolton-menk.com
(612) 430-2805

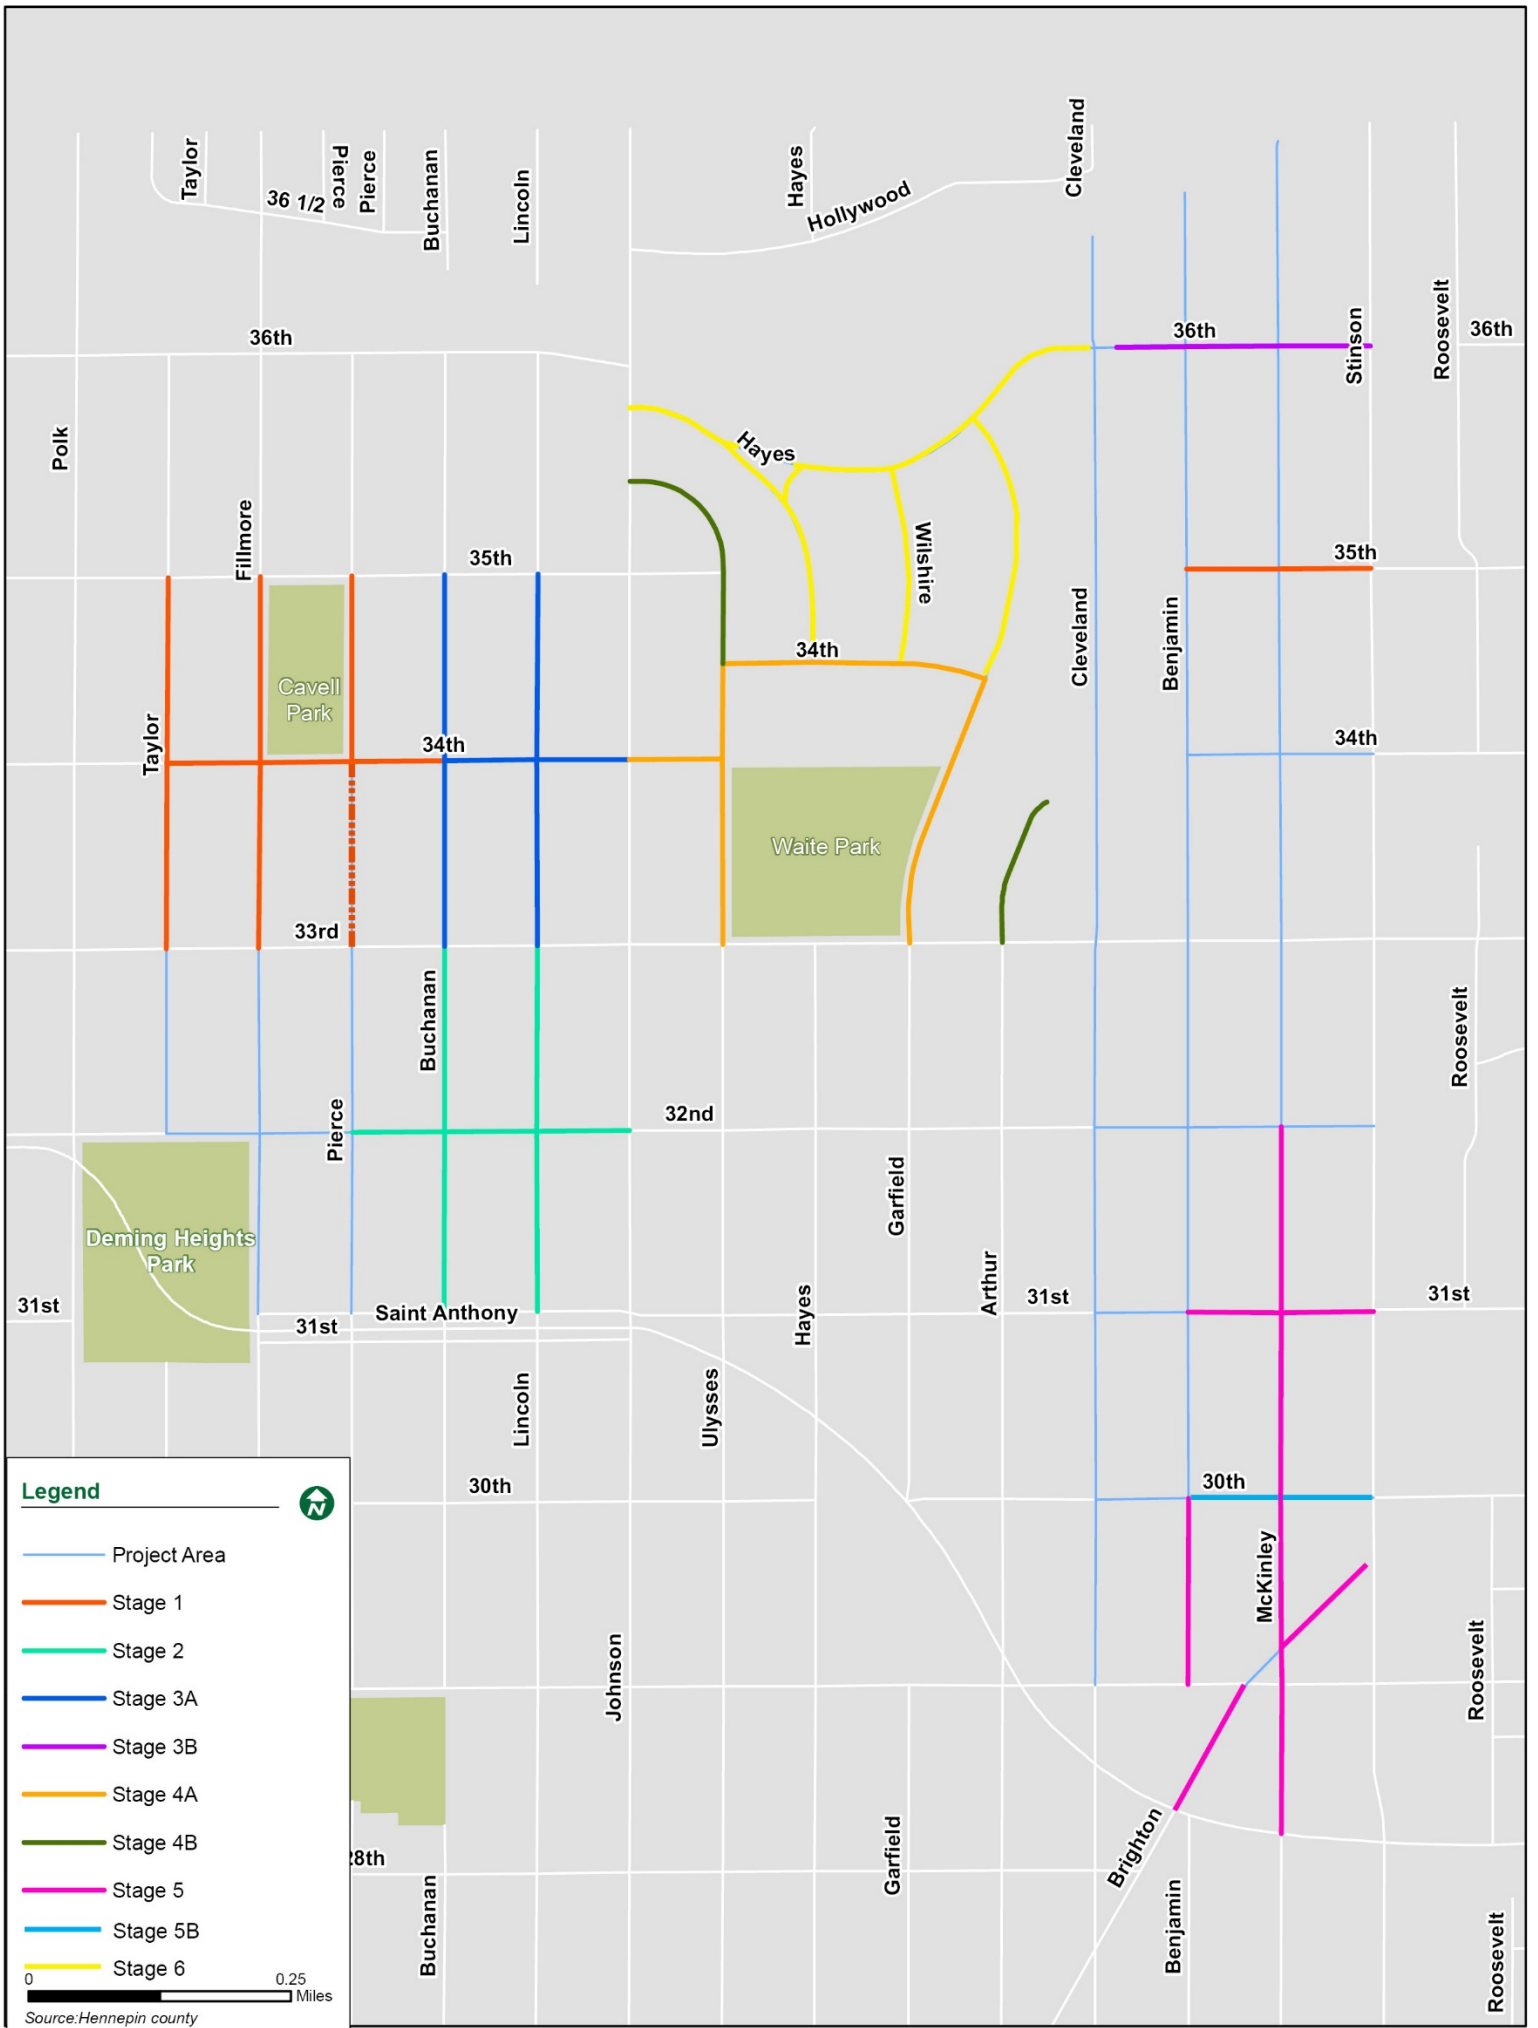

Legend

- Project Area
- Stage 1
- Stage 2
- Stage 3A
- Stage 3B
- Stage 4A
- Stage 4B
- Stage 5
- Stage 5B
- Stage 6

0 0.25 Miles

Source: Hennepin county
